EASTERN TUNNELLING PACKAGE
John Holland CPB Contractors Ghella JV

EPL 21784 POLLUTION MONITORING REPORT

June 2026

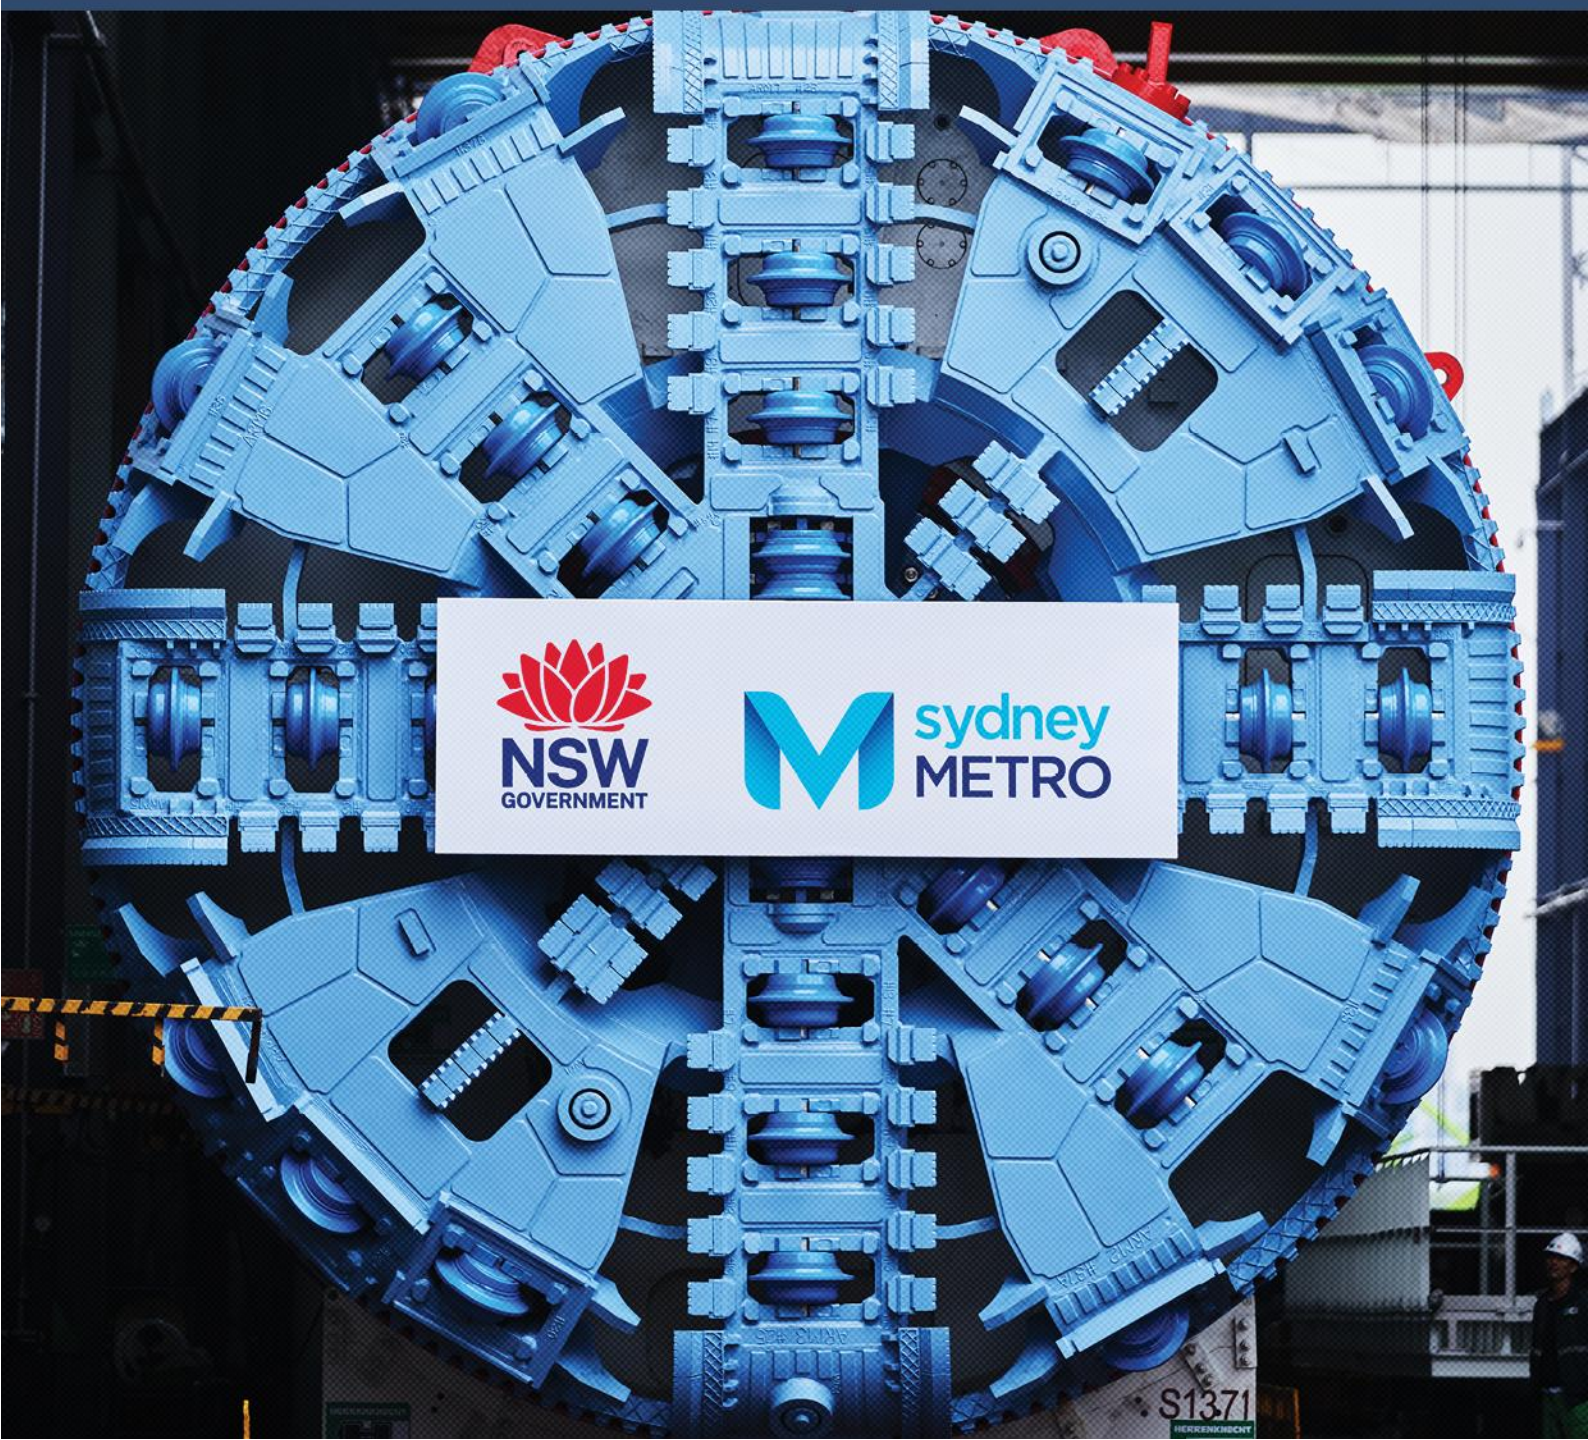

EPL 21784 POLLUTION MONITORING REPORT

June 2026

Project number	7040
Document number	SMWSTETP-JCG-SWD-SW000-EN-RPT-095163

Document approval

Rev	Date	Prepared by	Reviewed by	Comments	Approved by
[redacted]					
Signature:					

THIS PLAN IS THE PROPERTY OF JCG AND MAY NOT BE COPIED, DISTRIBUTED OR USED WITHOUT THE WRITTEN CONSENT OF THE JCG

Table of contents

1. Introduction 2
1.1. Project overview 2
1.2. Project Scope 3
1.3. Scope of this report 3
2. Reporting Requirements 4
3. Monitoring 7
3.1. Meteorological Data 7
3.2. Noise 7
3.3. Discharge to water 8
4. Correction Log 9
Appendix A Weather Data 10
Appendix B Noise Monitoring Results 12

1. Introduction

1.1. Project overview

Sydney Metro West (SMW) is a new 24-kilometre metro line with nine new stations confirmed at Westmead, Parramatta, Sydney Olympic Park, North Strathfield, Burwood North, Five Dock, The Bays, Pyrmont, and Hunter Street in the Sydney CBD.

The planning process for Sydney Metro West was assessed as a staged infrastructure application under section 5.20 of the *Environment Planning and Assessment Act 1979 (EP&A Act)*.

Stage 1 of the development, the Sydney Metro West Concept and major civil construction work for Sydney Metro West between Westmead and The Bays (SSI-10038 Schedule 2), was approved on 11 March 2021 and includes:

- Construction and operation of new passenger rail infrastructure between Westmead and the central business district of Sydney, including:
  - Tunnels, stations (including surrounding areas) and associated rail facilities
  - Stabling and maintenance facilities (including associated underground and overground connections to tunnels)
- Modification of existing rail infrastructure, including stations and surrounding areas
- Ancillary development.

The Eastern Tunnelling Package (ETP or this Project) is addressed under the Stage 2 Planning Approval (SSI 19238057). This Project includes all major civil construction work including station excavation (at the Pyrmont Station and Hunter Street Station (Sydney CBD) construction sites) and tunnelling between The Bays and Sydney CBD (Figure 1).

It is noted that the existing Sydney Metro West precast facility at Eastern Creek will be utilised in the delivery of the ETP Works. The facility, which was assessed by Sydney Metro in a Review of Environmental Factors (REF) and approved on 11 March 2021, is outside of the scope of the SWMP.

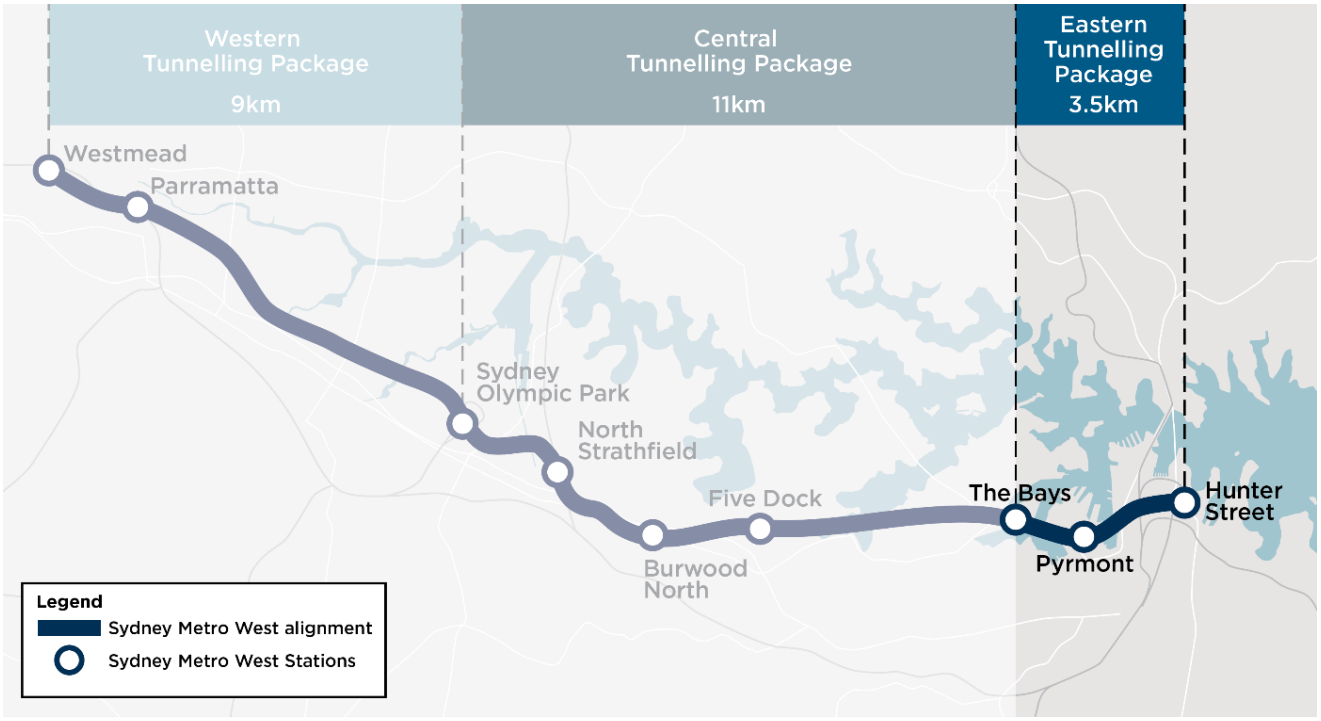

Figure 1: Sydney Metro West alignment

1.2. Project Scope

The ETP Works include design and construction of:

- Demolition of existing buildings at Pyrmont East and West shaft sites and at Hunter Street East and West shaft sites
- Tunnel Boring Machine (TBM) assembly, launch, tunnelling support from an existing shaft at The Bays
- Approximately 2.5 km twin underground eastbound and westbound bored railway tunnels between The Bays and Hunter Street and twelve cross passages spaced up to 250 metres apart
- Pyrmont Station excavation, including two shaft excavations, associated access adits and nozzle enlargements, including temporary ground support and cast in situ cavern linings
- Excavation and lining of a mined crossover cavern to allow trains to cross from one track to the other
- Hunter Street station mined cavern excavation, including:
  - Two shaft excavations, associated access adits
  - Nozzle enlargements
  - Conversion of an existing temporary connection adit at Bligh Street linking Hunter Street Station to Martin Place Station into a permanent pedestrian connection linking the stations (including temporary ground support and cast in situ linings)
- A turnback extension tunnel, of approximately 675 metres, east of the Hunter Street Station works to enable Sydney Metro train storage and to change tracks and travel direction (eastbound to westbound)
- TBM disassembly and retrieval from Hunter Street East.

1.3. Scope of this report

John Holland CPB Contactors Ghella (JCG) have been issued an Environmental Protection Licence (EPL No. 21784) from the NSW Environment Protection Authority (EPA) for the Sydney Metro West Eastern Tunnelling Package (ETP) Project.

The EPL applies to the works approved under the Infrastructure Approval SSI-19238057 associated with the delivery of the Sydney Metro West Eastern Tunnelling Package (ETP) Project.

This EPL Pollution Monitoring Report provides the results of all pollution monitoring required to be measured or monitored by the licensee of EPL 21784 as required by Section 66 of the Protection of the Environment Operations Act 1997 (POEO Act) and with reference to EPA Publication Requirements for publishing pollution monitoring data (Environment Protection Authority, 2013).

Table 1 provides a summary of the EPL 21784 details.

Table 1: Licence Details

Licence Details	
Number	21784
Copy of Licence	https://apps.epa.nsw.gov.au/prpoeoapp/ViewPOEOLicence.aspx?DOCID=266460&SYSUID=1&LICID=21784
Anniversary Date	16 March
Licensee	John Holland Pty Ltd
Premises	Sydney Metro West – Eastern Tunnelling Package
Scheduled Activity	Railway activities – railway infrastructure construction

2. Reporting Requirements

Under the POEO Act, holders of environment protection licences (licensees) must publish or make pollution monitoring data available to members of the public.

The POEO Act Section 66 requires:

> "66 Conditions requiring monitoring, certification or provision of information, and related offences
>
> (1) Monitoring The conditions of a licence may require—
>
> (a) monitoring by the holder of the licence of the activity or work authorised, required or controlled by the licence, including with respect to—
>
> (i) the operation or maintenance of premises or plant, and
>
> (ii) discharges from premises, and
>
> (iii) relevant ambient conditions prevailing on or outside premises,
>
> and
>
> (iv) anything required by the conditions of the licence, and
>
> (b) the provision and maintenance of appropriate measuring and recording devices for the purposes of that monitoring, and
>
> (c) the analysis, reporting and retention of monitoring data.
>
> (2) False or misleading information. A holder of a licence who supplies information, or on whose behalf information is supplied, to the appropriate regulatory authority under the conditions of the licence is guilty of an offence if the information is false or misleading in a material respect."

The primary objective of the pollution monitoring reporting requirements is that members of the public have access to the results of all pollution monitoring (which a licence specifies must be carried out) in a way that is meaningful to them. Data for the Sydney Metro West Eastern Tunnelling Package is presented on a monthly sampling period.

The monitoring data that must be published and/or made available on request is any data that is obtained as a result of a monitoring condition on a licence that relates to air, water (surface or groundwater), noise and/or land pollution. The data to be published or provided is limited to data that relates to pollutants generated, discharged or emitted from the licensed premises.

The data is provided in tabular format that is easy for the general public to understand. Tables definitively display raw data values, while graphs and charts are useful for overviews and visualisation of long-term trends. Raw data will be provided upon request.

An upfront note will be included on the licensee's website or in this report to explain why any data may appear to be missing because there is no discharge or the level of pollutant being below the detection level of the measurement instrument.

It is possible from time to time that incorrect data may be published in good faith. As soon as practicable after the licensee becomes aware that the published pollution monitoring data is incorrect or misleading, licensees must then publish a correction log to correct this data that is incorrect or misleading (refer to **Section 4).**

Table 2 provides a summary of the pollution monitoring requirements of EPL 21784.

Table 2: EPL 21784 Pollution Monitoring Requirements

<table>
<tr><th>EPL Condition</th><th>Requirement</th><th>Report Reference</th></tr>
<tr><td colspan="3">Weather</td></tr>
<tr><td>M5.1</td><td>The licensee must monitor and record temperature, humidity, wind direction, wind velocity and rainfall at either the project weather station, or through analysis of equivalent weather information obtained from the Australia Bureau of Meteorology. Monitoring must:
a) be representative of each catchment area;
b) commence prior to any works that may cause sediment to leave the premises; and
c) continue to be operated until soil disturbance activities cease at the premises and the site has been stabilised.</td><td>Section 3.1
Appendix A3.1</td></tr>
<tr><td colspan="3">Noise</td></tr>
<tr><td>L5.9</td><td>In undertaking any works and activities outside of standard construction hours under condition L5.8, the licensee must comply with the following:
a) Prepare a construction noise and vibration impact assessment in accordance with the Interim Construction Noise Guideline (DEC,2009) that is to include:
i. a description of the proposed works and activities outside of standard constructions hours;
ii. predictions of LAeq (15 minute) dB noise levels at noise sensitive receivers from these works and activities, where noise levels are predicted to be greater than those permitted under condition L5.3; and
iii. a monitoring plan to validate the noise predictions, based on monitoring at the boundary of representative sensitive receivers during noise generating activities that are representative of the works and activities, including during the period/s predicted to have the highest noise level impacts.
b) Undertake noise monitoring in accordance with the monitoring plan required by condition L5.9(a)(iii).</td><td>Section 3.2
Appendix B</td></tr>
<tr><td>M4.4</td><td>The licensee must undertake noise and vibration monitoring as directed by an authorised officer of the EPA. If a licensee is unable to obtain permission, they must provide the response to the EPA.</td><td>N/A</td></tr>
<tr><td colspan="3">Water</td></tr>
<tr><td>P1.1</td><td>The following points referred to in the table are identified in this licence for the purposes of the monitoring and/or the setting of limits for discharges of pollutants to water from the point.
<table>
<tr><th>EPA Identification no.</th><th>Type of Monitoring Point</th><th>Type of Discharge Point</th><th>Location Description</th></tr>
<tr><td>1</td><td>Discharge & Monitoring</td><td>Discharge & Monitoring</td><td>Discharge from the Hunter St Station WTP to Sydney Harbour</td></tr>
<tr><td>2</td><td>Discharge & monitoring</td><td>Discharge & monitoring</td><td>Discharge from the Eastern Creek Precast Facility sediment basin</td></tr>
<tr><td>6</td><td>Discharge & Monitoring</td><td>Discharge & Monitoring</td><td>Discharge from The Bays Construction WTP to White Bay</td></tr>
<tr><td>7</td><td>Discharge & Monitoring</td><td>Discharge & Monitoring</td><td>Discharge from Pyrmont East Surface Water Discharge</td></tr>
</table></td><td>Section 2</td></tr>
<tr><td>M2.1</td><td>For each monitoring/discharge point or utilisation area specified below (by a point number), the licensee must monitor (by sampling and obtaining results by analysis) the concentration of each pollutant specified in Column 1. The licensee must use the sampling method, units of measure, and sample at the frequency, specified opposite in the other columns.</td><td>Section 5</td></tr>
</table>

EPL Condition	Requirement	Report Reference
M2.2		Section 5

POINT 1

Pollutant	Units of measure	Frequency	Sampling Method
Aluminium	micrograms per litre	Monthly during discharge	Grab sample
Ammonia	micrograms per litre	Monthly during discharge	Grab sample
Arsenic (III)	micrograms per litre	Monthly during discharge	Grab sample
Cadmium	micrograms per litre	Monthly during discharge	Grab sample
Chromium (hexavalent)	micrograms per litre	Monthly during discharge	Grab sample
Cobalt	micrograms per litre	Monthly during discharge	Grab sample
Copper	micrograms per litre	Monthly during discharge	Grab sample
Iron	micrograms per litre	Monthly during discharge	Grab sample
Manganese	micrograms per litre	Monthly during discharge	Grab sample
Nitrate	micrograms per litre	Monthly during discharge	Grab sample
Nitrogen (total)	micrograms per litre	Monthly during discharge	Grab sample
Oil and Grease	Visible	Monthly during discharge	Visual Inspection
pH	pH	Daily during any discharge	Probe
Phosphorus (total)	micrograms per litre	Monthly during discharge	Grab sample
TRH C10-C14	micrograms per litre	Monthly during discharge	Grab sample
TSS	milligrams per litre	Monthly during discharge	Grab sample
Zinc	micrograms per litre	Monthly during discharge	Grab sample

POINT 2

Pollutant	Units of measure	Frequency	Sampling Method
Oil and Grease	Visible	Special Frequency 1	Visual Inspection
pH	pH	Special Frequency 1	Probe
TSS	milligrams per litre	Special Frequency 1	Grab sample

POINT 6

Pollutant	Units of measure	Frequency	Sampling Method
Aluminium	micrograms per litre	Monthly during discharge	Grab sample
Ammonia	micrograms per litre	Monthly during discharge	Grab sample
Arsenic	micrograms per litre	Monthly during discharge	Grab sample
Cadmium	micrograms per litre	Monthly during discharge	Grab sample
Chromium (hexavalent)	micrograms per litre	Monthly during discharge	Grab sample
Cobalt	micrograms per litre	Monthly during discharge	Grab sample
Copper	micrograms per litre	Monthly during discharge	Grab sample
Iron	micrograms per litre	Monthly during discharge	Grab sample
Lead	micrograms per litre	Monthly during discharge	Grab sample
Manganese	micrograms per litre	Monthly during discharge	Grab sample
Mercury	micrograms per litre	Monthly during discharge	Grab sample
Nickel	micrograms per litre	Monthly during discharge	Grab sample
Nitrate + nitrite (oxidised nitrogen)	micrograms per litre	Monthly during discharge	Grab sample
Nitrogen (total)	micrograms per litre	Monthly during discharge	Grab sample
Oil and Grease	Visible	Monthly during discharge	Visual Inspection
pH	pH	Daily during any discharge	Probe
Phosphorus (total)	micrograms per litre	Monthly during discharge	Grab sample
TPH > C10-C40 (sum) Fraction	micrograms per litre	Monthly during discharge	Grab sample
TSS	milligrams per litre	Monthly during discharge	Grab sample
Zinc	micrograms per litre	Monthly during discharge	Grab sample

EPL Condition	Requirement	Report Reference
	POINT 7	

Pollutant	Units of measure	Frequency	Sampling Method
Oil and Grease	Visible	Monthly during discharge	Visual Inspection
pH	pH	Monthly during discharge	Probe
TSS	milligrams per litre	Monthly during discharge	Grab sample

3. Monitoring

Section 3 presents a summary of the monitoring programs completed in the reporting period from 16 May 2026 to 16 June 2026.

Detailed monitoring results for each program are presented in the Appendices.

3.1. Meteorological Data

Meteorological data for the Project has been mostly taken from the Observatory Hill station, but some has also been taken from Fort Denison and Sydney Airport, Bureau of Meteorology Weather Station.

The total rainfall recorded during the reporting period was 97.4 mm, with 14 days exceeding 1mm and 4 days exceeding 10mm.

During the reporting period, there were 21 days where the maximum wind gust recorded was greater than 25km/h, 6 days where the maximum wind gust recorded was greater than 50km/h and 1 day where the maximum wind gust recorded was greater than 60km/h. Winds recorded during the reporting period were predominantly westerly in the morning and predominantly easterly in the afternoons.

A summary of the weather observations and weather events during the reporting period of relevance to the Soil and Water Management Sub-plan and Air Quality Management Sub-Plan Trigger Action Response Plans (TARPs) are summarised in Table 3.

Detailed weather observation records for the reporting period are presented in Appendix A.

Table 3: Weather summary and trigger weather events for the reporting period.

Weather Event	Observation
Minimum temperature	9.1 °C
Maximum temperature	23.8 °C
Total rainfall	97.4 mm
Number of days with rain (>1 mm)	14 days
Number of days with rain (>10 mm)	4 days
>25 km/hr wind	21 days
>50 km/hr wind	6 days
>60 km/hr wind	1 day

3.2. Noise

Table 4: Summary of noise and vibration monitoring completed during the reporting period

Date	Monitoring Location	Method	Description
02/06/2026	Pyrmont East	Sound Level Meter	Hammering of invert (Pyrmont East shaft nozzles)
03/06/2026	Eastern Creek	Sound Level Meter	Eastern Creek pre-cast facility (site operation)
15/06/2026	Hunter Street (East)	Sound Level Meter	Service Disconnection (Sydney Water)

3.3. Discharge to water

Discharge water quality monitoring is a requirement of the following conditions of EPL 21784:

- L2.1 For each monitoring/discharge point, the concentration of a pollutant discharged at that point, must not exceed the concentration limits specified for that pollutant in the table
- M2.1 For each monitoring/discharge point, the licensee must monitor (by sampling and obtaining results by analysis) the concentration of each pollutant specified in Column 1. The licensee must use the sampling method, units of measure, and sample at the frequency specified opposite in the other columns.

During the reporting period sampling was undertaken from:

- EPL Point 2 – Discharge from Eastern Creek Precast Facility sediment basin (refer to Table 5)
- EPL Point 6 – Discharge from The Bays WTP (refer to Table 6).

Discharge from Hunter Street Construction WTP was directed to Trade Waste during the reporting period.

Table 5: Concentration of pollutants discharged from Point 2 during the reporting period

Date			Sample taken 03/06/2026
Pollutant	**Units**	**Criteria**	**Discharge**
Oil and Grease	Visible	Not Visible	Not Visible
pH	pH	6.5 – 8.5	8.3
TSS	NTU	50	<5

Table 6: Concentration of pollutants discharged from Point 6 during the reporting period

Date			Sample taken 28/05/2026
Pollutant	**Units**	**Criteria**	**Discharge**
Aluminium	(µg/L)	250	20
Ammonia	(µg/L)	910	260
Arsenic	(µg/L)	4.5	<1
Cadmium	(µg/L)	0.7	<0.1
Chromium (hexavalent)	(µg/L)	20	<5
Cobalt	(µg/L)	1.4	<1
Copper	(µg/L)	2	<1
Iron	(µg/L)	700	<10
Lead	(µg/L)	4.4	<1
Manganese	(µg/L)	1900	<5
Mercury	(µg/L)	0.1	<0.05
Nickel	(µg/L)	70	1
Nitrate	(µg/L)	660	240
Nitrogen (Total)	(µg/L)	1720	1,400
Oil and Grease	Visible	Not Visible	Not visible
pH	pH	7.0-8.5	8.3
Phosphorus (total)	(µg/L)	140	<50
TPH>C10 – C40 (sum)	(µg/L)	100	<50

Date			Sample taken 28/05/2026
Pollutant	**Units**	**Criteria**	**Discharge**
TSS	(mg/L)	15	<5
Zinc	(µg/L)	15	<1

4. Correction Log

It is possible from time to time for incorrect data to get published in good faith.

As soon as practicable after the licensee becomes aware that the published pollution monitoring data is incorrect or misleading, licensees must then publish a correction log to correct this data that is incorrect or misleading.

There are no matters included in the correction log for this reporting period.

Appendix A Weather Data

Table 7: Weather Observations. Temperature and Relative Humidity. Observatory Hill BOM Station.

Date	Min temperature (°C)	Max temperature (°C)	Rainfall (mm)	9am Temperature (°C)	9am relative humidity (%)	3pm Temperature (°C)	3pm relative humidity (%)
15/05/2026	14.2	22.1	12.6	16.2	95	21.6	68
16/05/2026	14.8	23.3	0.2	17.1	93	21.8	69
17/05/2026	16.4	20.3	1.2	17.8	91	20.2	76
18/05/2026	16.1	19.1	0.2	16.9	93	18.9	82
19/05/2026	16.3	21.7	10.0	17.9	91	19.8	72
20/05/2026	11.5	20.0	2.6	16.1	63	19.0	43
21/05/2026	11.9	20.0	0	14.9	66	19.1	61
22/05/2026	12.9	20.8	2.0	15.1	89	16.7	86
23/05/2026	14.4	20.6	4.0	17.6	80	18.0	91
24/05/2026	14.6	20.5	3.4	16.2	97	19.6	75
25/05/2026	16.1	21.2	6.6	17.5	96	18.9	92
26/05/2026	17.4	20.7	7.4	18.1	95	19.9	91
27/05/2026	15.8	23.2	15.0	17.2	96	22.5	67
28/05/2026	17.1	21.1	13.6	18.6	94	19.6	91
29/05/2026	16.5	21.2	11.8	16.6	92	20.5	65
30/05/2026	12.1	21.6	0	13.4	62	19.5	47
31/05/2026	11.3	20.5	0	14.9	66	19.5	39
01/06/2026	9.3	18.7	0	13.3	58	18.3	40
02/06/2026	11.7	18.2	1	15.0	52	14.8	72
03/06/2026	14.2	21.3	0.6	18.2	56	20.1	37
04/06/2026	13.2	19.2	0	15.9	59	19.0	44
05/06/2026	11.5	19.0	0	13.9	60	17.4	44
06/06/2026	9.1	19.9	0	12.3	62	19.5	41
07/06/2026	9.6	20.6	0	12.8	66	20.0	48
08/06/2026	9.8	21.2	0	13.0	82	18.3	67
09/06/2026	12.0	21.5	0	14.8	91	18.9	67
10/06/2026	13.7	23.5	0	17.6	72	22.1	65
11/06/2026	15.8	21.6	1.6	16.2	92	19.6	72
12/06/2026	15.2	21.7	0	16.4	85	19.8	76
13/06/2026	14.5	23.8	0	16.9	92	21.2	67
14/06/2026	16.3	21.4	0	16.3	84	20.8	73
15/06/2026	15.9	nd	3.6	16.9	75	18.1	62
16/06/2026	nd	nd	nd	nd	nd	nd	nd

Note: nd = no data available

Table 8: Wind Observations. Observatory Hill BOM Station.

Date	Direction of max wind gust	Speed of max wind gust (km/h)	Time of max wind gust	9am wind direction	9am wind speed (km/h)	3pm wind direction	3pm wind speed (km/h)
15/05/2026	ESE	24	14:05	WNW	11	ESE	13
16/05/2026	NNE	30	22:04	WNW	13	E	17
17/05/2026	WNW	15	01:26	NNW	6	N	6
18/05/2026	WNW	24	08:06	W	15	Calm	Calm
19/05/2026	SSW	50	16:09	WNW	13	S	19
20/05/2026	W	41	23:41	W	19	SSE	24
21/05/2026	S	56	12:55	W	22	SSW	28
22/05/2026	nd	Nd	nd	W	17	nd	nd
23/05/2026	SSE	35	13:13	WSW	7	S	11
24/05/2026	W	22	01:20	WNW	7	E	6
25/05/2026	WNW	15	04:16	WNW	13	ESE	6
26/05/2026	WNW	22	07:11	NW	4	ESE	13
27/05/2026	W	20	07:25	W	17	ESE	4
28/05/2026	SSW	39	11:31	SSW	19	SSW	17
29/05/2026	SW	46	09:48	SW	20	SSW	24
30/05/2026	WSW	41	10:33	W	22	W	20
31/05/2026	W	46	10:41	WNW	17	W	26
01/06/2026	W	33	00:06	W	13	NW	11
02/06/2026	NW	63	14:20	NNW	33	N	41
03/06/2026	WNW	54	14:39	NNW	19	WNW	37
04/06/2026	NW	43	15:25	NNW	13	NW	22
05/06/2026	W	50	10:45	W	26	SSW	17
06/06/2026	W	35	09:00	W	24	WNW	7
07/06/2026	W	31	03:04	W	20	ESE	7
08/06/2026	WNW	22	00:22	WNW	17	E	9
09/06/2026	NE	28	14:38	W	9	NE	19
10/06/2026	N	26	11:11	NNE	6	NE	13
11/06/2026	SSW	31	14:09	WNW	11	S	19
12/06/2026	SW	26	10:51	WNW	15	S	11
13/06/2026	ENE	20	13:49	NNW	9	NE	11
14/06/2026	SW	50	15:34	W	22	WNW	7
15/06/2026	nd	nd	nd	SSE	13	ENE	11
16/06/2026	nd	nd	nd	nd	nd	nd	nd

Note: nd = no data available

Appendix B Noise Monitoring Results

Table 9: Noise Monitoring Results

Date	Time	Works Period	Construction Activity	Activity Location	Monitoring Location	NML (dBA)	Predicted* (dBA)	Recorded Leq (dBA)	LAmax	Exceedance of Predicted (dBA)	Exceedance of Predicted	Comments
Attended noise monitoring												
02/06/2026	15:15	Day	Hammering of invert with a 14T excavator (Pyrmont's shaft nozzles)	Pyrmont East	1-9 Pyrmont Bridge Road, Pyrmont	62	-	69.5	85.0	-	-	Ground-borne noise monitoring during standard working hours. Constant traffic noise at Pyrmont Bridge Road during whole monitoring period. Hammering almost inaudible (around 61 dB). Windy condition during noise monitoring.
03/06/2026	15:19	Day	Pre-cast facility / Site operation	Eastern Creek	6 Weaver Street, Pyrmont	47	39	55.2	74.8	16.2	Yes	Dominant noise source was traffic from Swallow Drive and windy conditions. Site operations were inaudible during noise monitoring event.
15/06/2026	20:12	Evening	Service Disconnection (Sydney Water)	Hunter East	16 O'Connell Street	67	76	71.1	89	N/A	No	Other sources of noise contributed to noise levels registered during monitoring such as cars and buses passing by. Noise mitigation measures were in place during monitoring (noise blankets)
15/06/2026	20:40	Evening	Service Disconnection (Sydney Water)	Hunter East	27 O'Connell Street	65	82	84.7	89.3	2.7	Yes	Other sources of noise contributed to noise levels registered during monitoring such as cars and buses passing by. Works non-Project related being carried out at Hunter Street (road saw being used). Noise mitigation measures were in place during monitoring (noise blankets).

Table 10: Current location of all real time noise and vibration monitors

Date	Time	Construction Activity	Activity location	Monitoring location	NML (dBA)*	*Predicted (dBA)	*Recorded Leq, 15min (dBA)	* LAmax	*Exceedance of Predicted (dBA)	Exceedance of Predicted *	Comments
+Real time noise and vibration monitoring											
	Continuous	Construction – Noise	Pyrmont East	69 - 71 Edward Street, Pyrmont, 2009	*	*	*	*	*	*	
	Continuous	Construction – Noise	Hunter Street West	10 Hunter Street	*	*	*	*	*	*	
	Continuous	Construction – Noise	Hunter Street West	The Ivy 320/330 George Street (Level 2 Office Printer Room)	*	*	*	*	*	*	
	Continuous	Construction – Noise	Hunter Street East	Level 12, 16 O'Connell Street	*	*	*	*	*	*	
	Continuous	Construction - Noise	Hunter Street East	Paradox Sydney Hotel (Level 1) 27 O'Connell Street Sydney NSW	*	*	*	*	*	*	
	Continuous	Construction – Noise	Hunter Street East	Hunter East hoarding (within site boundary)	*	*	*	*	*	*	
	Continuous	Construction - Noise	Hunter Street West	Hunter Street West (within site boundary)	*	*	*	*	*	*	
	Continuous	Construction – Vibration	Hunter Street West	The Ivy (Basement)	*	*	*	*	*	*	
	Continuous	Construction – Vibration	Hunter Street West	The Skinners Hotel (Level 3 South, 296 George Street)	*	*	*	*	*	*	
	Continuous	Construction – Vibration	Hunter Street East	16 O'Connell Street	*	*	*	*	*	*	
	Continuous	Construction – Vibration	Hunter Street West	Tank Stream	*	*	*	*	*	*	
	Continuous	Construction – Vibration	Hunter Street East	Lowy Institute VIB	*	*	*	*	*	*	
	Continuous	Construction – Vibration	Hunter Street East	25 Bligh Street	*	*	*	*	*	*	
	Continuous	Construction – Vibration	Hunter Street East	Arcade Bar, 16 O'Connell Street	*	*	*	*	*	*	

Date	Time	Construction Activity	Activity location	Monitoring location	NML (dBA)*	* Predicted (dBA)	* Recorded Leq, 15min (dBA)	* LAmax	* Exceedance of Predicted (dBA)	Exceedance of Predicted *	Comments
+Real time noise and vibration monitoring											
	Continuous	Construction – Vibration	Hunter Street West	Pangas House, 15-17 Hunter Street	*	*	*	*	*	*	
	Continuous	Construction – Vibration	Hunter Street East	109 Pitt Street	*	*	*	*	*	*	
	Continuous	Construction - Vibration	Hunter Street	Lowey Institute	*	*	*	*	*	*	
	Continuous	Construction - Vibration	Hunter Street East	27 Hunter Street	*	*	*	*	*	*	
